

## Status of Project Schedule




March 16, 2005

## Efforts in January/February 2005

- ◆ **Compiled Information to be used in Alternatives Development and Evaluation**
  - ☒ Update Existing Baseline Conditions Report
  - ☒ Range of Inflows and Water Quality Conditions
  - ☒ Draft Selenium Assessment Reports
  - ☒ Draft Air Quality Assessment Report
  - ☒ Preparing for Quarry field exploration
- ◆ **Developed Design Criteria for Development of Alternatives**
- ◆ **Conducted Seven Public Meetings**

## Overall Schedule

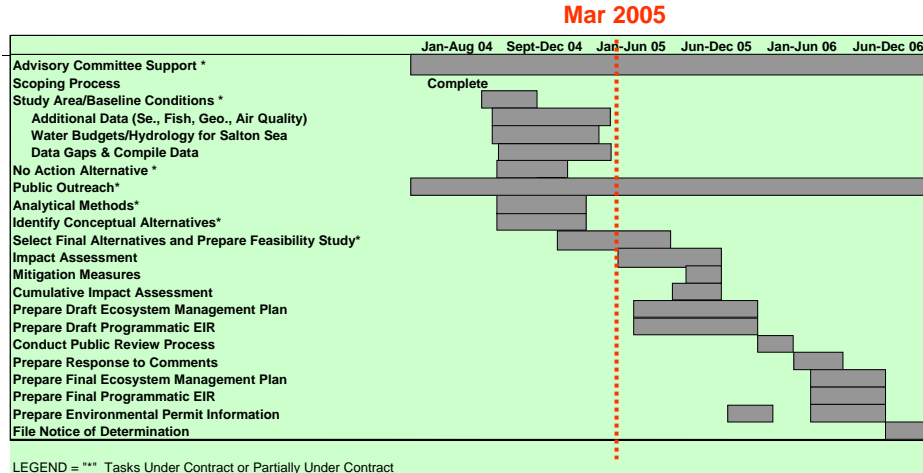

## Efforts Planned for March-May 2005

### ◆ Initiate Field Work for Water Quality and Air Quality Tasks

- ☒ Sediment and water quality sampling
- ☒ Fish sampling
- ☒ Air monitoring and wind tunnel tests

### ◆ Develop Detailed Descriptions of Wide Range of Alternatives

- ☒ Layouts of facilities and habitats
- ☒ Cost estimates for capital and operations costs
- ☒ Initiate preparation of Feasibility Study for Salton Sea Ecosystem Restoration Plan

### ◆ Public Meetings in April
